TD Centre Redevelopment

3 Week Look-Ahead Schedule

Issued: Wed 5/01/13

ID	Task Name	Baseline Start	Baseline Finish	Projected Duration	Projected Start	Projected Finish
1	**Excavation**	**Tue 3/05/13**	**Mon 3/18/13**	**1 day**	**Wed 4/10/13**	**Wed 4/10/13**
2	Install new 8" storm water line	Wed 4/10/13	Wed 4/10/13	1 day	Wed 4/10/13	Wed 4/10/13
3	**Concrete - Footings, Shear Walls and Columns**	**Tue 2/26/13**	**Thu 3/21/13**	**30 days**	**Mon 4/08/13**	**Fri 5/17/13**
4	Level 1 - Place reinforcing steel for shear walls and columns	Mon 4/01/13	Fri 4/19/13	15 days	Mon 4/08/13	Fri 4/26/13
5	Level 1 - Form & pour concrete shear wall at Gridline A	Mon 4/08/13	Thu 4/11/13	4 days	Mon 4/08/13	Thu 4/11/13
6	Level 1 - Form & pour concrete shear wall at Gridline E	Wed 4/03/13	Mon 4/08/13	4 days	Wed 4/10/13	Mon 4/15/13
7	Level 1 - Form & pour concrete shear wall at Gridline 5 & elevator core	Mon 4/08/13	Fri 4/12/13	12 days	Mon 4/15/13	Tue 4/30/13
8	Level 2 - Mechanical Room - Form suspended slab	Tue 4/16/13	Tue 4/23/13	9 days	Tue 4/16/13	Fri 4/26/13
9	Level 2 - Place reinforcing steel for suspended slab	Tue 4/23/13	Thu 4/25/13	2 days	Mon 4/29/13	Tue 4/30/13
10	Level 2 - Mechanical Room - Pour concrete for suspended slab	Thu 4/25/13	Fri 4/26/13	1 day	Tue 4/30/13	Tue 4/30/13
11	Level 2 - Form 4ft riser wall & suspended slab	Tue 4/30/13	Thu 5/02/13	2 days	Wed 5/01/13	Thu 5/02/13
12	Level 2 - Place reinforcing steel for 4ft riserwall & suspended slab	Thu 5/02/13	Fri 5/03/13	2 days	Thu 5/02/13	Fri 5/03/13
13	Level 2 - Pour concrete for 4ft riser wall & suspended slab	Mon 5/06/13	Mon 5/06/13	1 day	Mon 5/06/13	Mon 5/06/13
14	Level 2- Place reinforcing steel for shear walls and columns	Mon 5/06/13	Fri 5/17/13	10 days	Mon 5/06/13	Fri 5/17/13
15	Level 2 - Form & pour concrete shear wall at Gridline A	Tue 5/07/13	Wed 5/08/13	2 days	Tue 5/07/13	Wed 5/08/13
16	Level 2 - Form & pour concrete shear wall at Gridline E	Thu 5/09/13	Fri 5/10/13	2 days	Thu 5/09/13	Fri 5/10/13
17	Level 2 - Form & pour concrete shear wall at Gridline 5 & elevator core	Mon 5/13/13	Fri 5/17/13	5 days	Mon 5/13/13	Fri 5/17/13
18	Form & pour 3 columns & shear wall in basement to underside of Level 1	Mon 5/06/13	Wed 5/08/13	3 days	Mon 5/06/13	Wed 5/08/13
19	**Mechanical**	**Mon 3/04/13**	**Sat 3/16/13**	**40 days**	**Mon 4/22/13**	**Fri 6/14/13**
20	Install sleeves in shear walls and suspended slabs	Mon 4/22/13	Fri 4/26/13	5 days	Mon 4/22/13	Fri 4/26/13
21	Level 2 - Air Handling Units Delivery	Mon 4/22/13	Mon 4/22/13	1 day	Mon 4/22/13	Mon 4/22/13
22	Level 2 - Mechanical Room - Set Air Handling Unit	Wed 5/15/13	Wed 5/15/13	1 day	Wed 5/15/13	Wed 5/15/13
23	Level 2 - Mechanical Room - Set Chillers	Wed 5/15/13	Wed 5/15/13	1 day	Wed 5/15/13	Wed 5/15/13
24	Level 2 - Mechanical Rough-in -	NA	NA	40 days	Mon 4/22/13	Fri 6/14/13
25	Sub-Basement - De-comission AHU's	Thu 5/02/13	Fri 5/03/13	2 days	Thu 5/02/13	Fri 5/03/13
26	**Electrical**	**Sat 3/16/13**	**Sun 3/17/13**	**24 days**	**Wed 4/24/13**	**Mon 5/27/13**
27	Power Shut Down - For new shear wall	Tue 4/30/13	Tue 4/30/13	1 day	Tue 4/30/13	Tue 4/30/13
28	Level 4, 5 & 6 - Disconnect / Prepare for Demolition	Wed 4/24/13	Mon 4/29/13	4 days	Wed 4/24/13	Mon 4/29/13
29	Sub-Basement - De-comission AHU's	Thu 5/02/13	Fri 5/03/13	2 days	Thu 5/02/13	Fri 5/03/13
30	NSPI - Change Switches & Transformers in Sub-basement	Mon 5/20/13	Mon 5/27/13	6 days	Mon 5/20/13	Mon 5/27/13
31	**Demolition**	**Mon 3/04/13**	**Thu 3/28/13**	**28 days**	**Mon 4/15/13**	**Wed 5/22/13**
32	NIGHT SHIFT - Remove panels on East side	Mon 4/22/13	Fri 5/17/13	20 days	Mon 4/22/13	Fri 5/17/13
33	Level 4 - Demolition & Abatement of vacant suites	Mon 4/22/13	Wed 5/22/13	21 days	Wed 4/24/13	Wed 5/22/13
34	Level 5 - Demolition & Abatement of vacant suites	Mon 4/15/13	Mon 5/20/13	21 days	Mon 4/15/13	Mon 5/13/13
35	Level 6 - Demolition & Abatement of vacant suites	Wed 4/24/13	Wed 5/22/13	21 days	Wed 4/24/13	Wed 5/22/13
36	Sub-Basement - Demolish AHU's	Mon 5/06/13	Mon 5/13/13	6 days	Mon 5/06/13	Mon 5/13/13
37	**Unitized Curtain Wall System**	**NA**	**NA**	**17 days**	**Thu 5/02/13**	**Fri 5/24/13**
38	Level 2 & 3 - Layout for curtain wall system	Thu 5/02/13	Fri 5/03/13	2 days	Thu 5/02/13	Fri 5/03/13
39	Level 2 & 3 - Deliver of unitized units	Mon 5/06/13	Tue 5/07/13	2 days	Mon 5/06/13	Tue 5/07/13
40	Level 2 & 3 - Remove & install new unitized curtain wall system	Mon 5/13/13	Fri 5/24/13	10 days	Mon 5/13/13	Fri 5/24/13

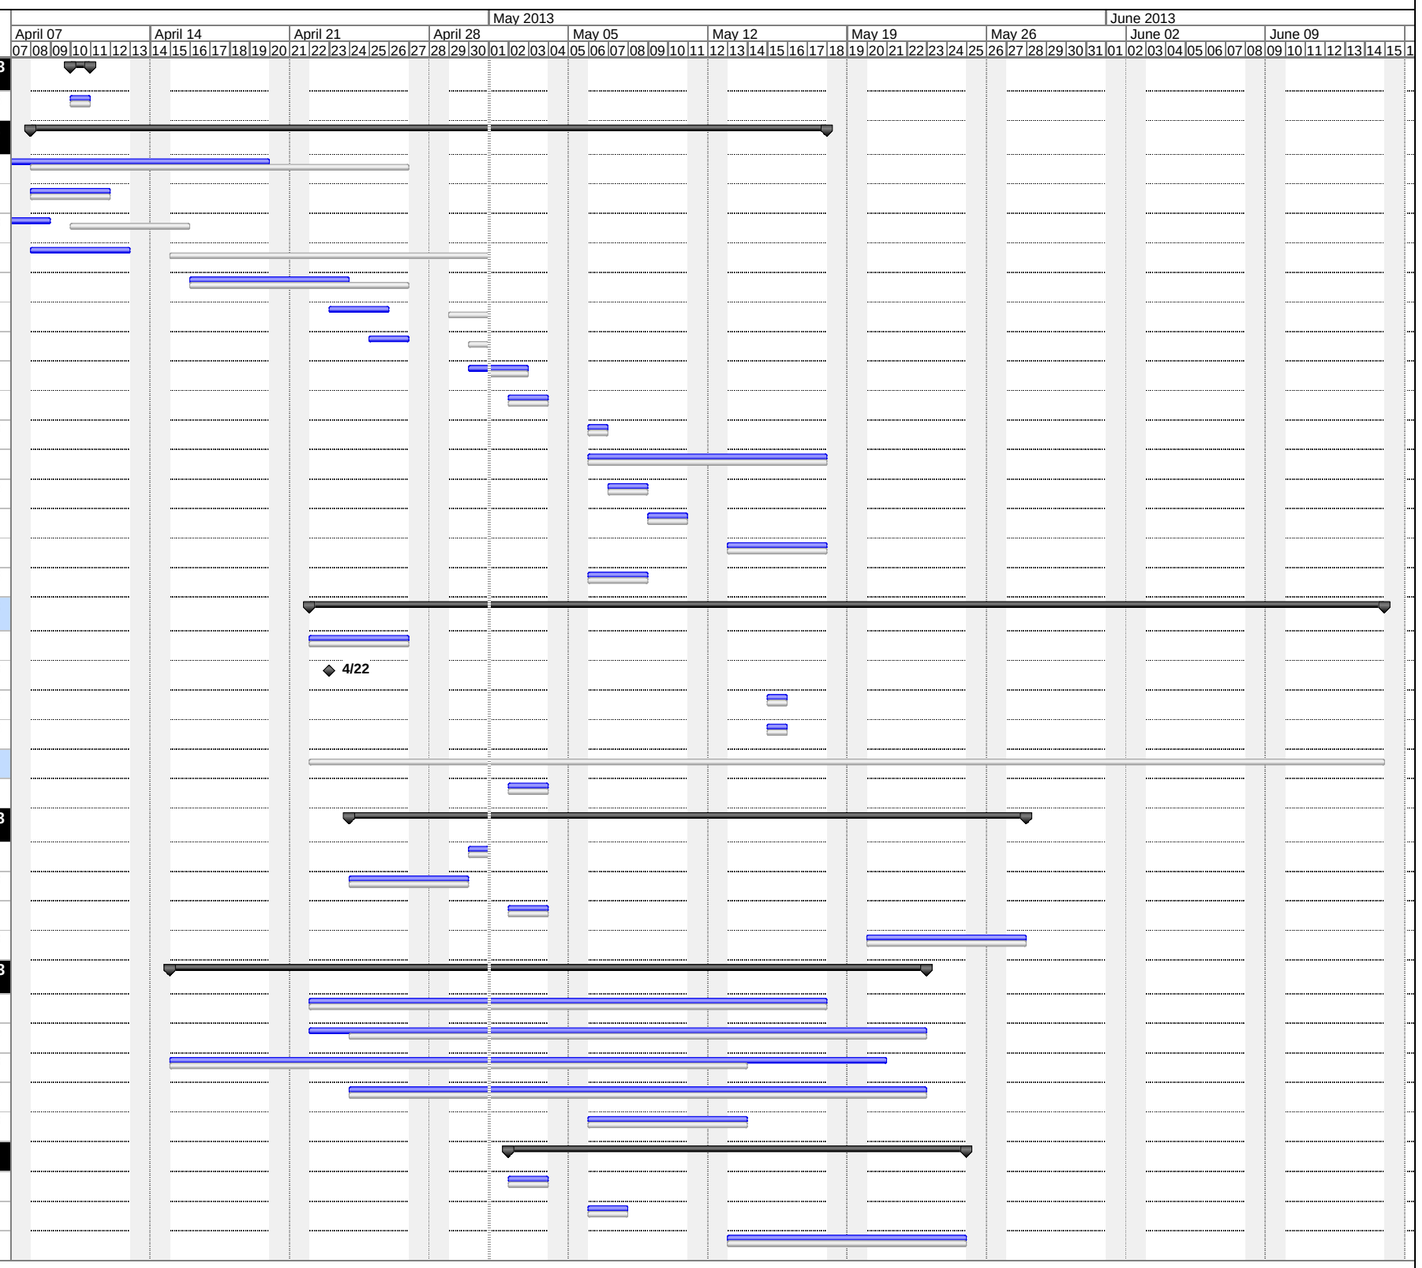

EllisDon
We build on great relationships™

Baseline Task | Actual Progress | Milestone | Summary

Wed 5/01/13
