TD Centre Redevelopment

3 Week Look-Ahead Schedule

Issued: Wed 3/20/13

ID	Task Name	Baseline Start	Baseline Finish	Projected Duration	Projected Start	Projected Finish
1	**Excavation**	**Tue 3/05/13**	**Mon 3/18/13**	**16 days**	**Tue 3/05/13**	**Mon 3/25/13**
2	Interior excavation for footing at Gridline H2 / 6.5	Tue 3/05/13	Tue 3/19/13	13 days	Tue 3/05/13	Wed 3/20/13
3	Excavation for foundation at Gridline 9.7 to 10 (E to C8)	Mon 3/18/13	Mon 3/25/13	6 days	Mon 3/18/13	Mon 3/25/13
4	**Concrete - Footings, Shear Walls and Columns**	**Tue 2/26/13**	**Thu 3/21/13**	**45 days**	**Tue 2/26/13**	**Fri 4/26/13**
5	Form & pour concrete shear wall at Gridline 5 (to underside of Level 1)	Tue 2/26/13	Tue 3/12/13	20 days	Tue 2/26/13	Fri 3/22/13
6	Form & pour concrete shear wall at Gridline E (Level 1)	Fri 3/01/13	Tue 3/05/13	17 days	Fri 3/01/13	Fri 3/22/13
7	Place reinforcing steel in shear walls (to underside of Level 1)	Wed 2/27/13	Tue 3/12/13	18 days	Wed 2/27/13	Thu 3/21/13
8	Form suspended slab at Level 1	Mon 3/11/13	Fri 3/15/13	16 days	Thu 3/14/13	Wed 4/03/13
9	Place reinforcing steel for suspended slab at Level 1	Sat 3/16/13	Mon 3/18/13	2 days	Wed 4/03/13	Thu 4/04/13
10	Pour concrete for suspended slab at Level 1	Tue 3/19/13	Tue 3/19/13	7 days	Thu 3/28/13	Fri 4/05/13
11	Place reinforcing steel for shear walls and columns (Level 2)	Mon 4/01/13	Fri 4/19/13	15 days	Mon 4/08/13	Fri 4/26/13
12	Form & pour concrete shear wall at Gridline A (Level 2)	Mon 3/18/13	Thu 3/21/13	4 days	Mon 4/08/13	Thu 4/11/13
13	Form & pour concrete shear wall at Gridline E (Level 2)	Wed 4/03/13	Mon 4/08/13	4 days	Wed 4/10/13	Mon 4/15/13
14	Form & pour concrete shear wall at Gridline 5 & elevator core (Level 2)	Mon 4/08/13	Fri 4/12/13	10 days	Mon 4/15/13	Fri 4/26/13
15	Place reinforcing steel for remaining columns 9.7(G) , 9.2(F7)	Tue 3/12/13	Thu 3/14/13	3 days	Wed 3/20/13	Fri 3/22/13
16	Form & pour remaining columns at ground level 9.7(G) , 9.2 (F7)	Tue 3/12/13	Fri 3/15/13	3 days	Wed 3/20/13	Fri 3/22/13
17	**Mechanical**	**Mon 3/04/13**	**Sat 3/16/13**	**19 days**	**Mon 3/04/13**	**Wed 3/27/13**
18	Install underground plumbing (connection to existing main service)	Mon 3/04/13	Fri 3/15/13	16 days	Mon 3/04/13	Fri 3/22/13
19	Relocate existing heating line at Gridline 4y / Fx	Thu 3/14/13	Fri 3/15/13	2 days	Thu 3/14/13	Fri 3/15/13
20	Level 2 & 3 - Disconnect / Prepare for Demolition	Mon 3/25/13	Wed 3/27/13	3 days	Mon 3/25/13	Wed 3/27/13
21	**Electrical**	**Sat 3/16/13**	**Sun 3/17/13**	**10 days**	**Sat 3/23/13**	**Fri 4/05/13**
22	WEEKEND - Relocate MCC panel in Sub basement	Sat 3/16/13	Sun 3/17/13	1 day	Sat 3/23/13	Mon 3/25/13
23	Install disconnect and breaker for Tower Crane	Mon 4/01/13	Mon 4/01/13	1 day	Mon 4/01/13	Mon 4/01/13
24	Prepare temporary bus duct feeders	Mon 4/01/13	Fri 4/05/13	5 days	Mon 4/01/13	Fri 4/05/13
25	Level 2 & 3 - Disconnect / Prepare for Demolition	Mon 3/25/13	Thu 3/28/13	4 days	Mon 3/25/13	Thu 3/28/13
26	**Demolition**	**Mon 3/04/13**	**Thu 3/28/13**	**26 days**	**Mon 3/04/13**	**Fri 4/05/13**
27	NIGHT SHIFT - Remove panels on East side to underside of Level 3	Mon 3/11/13	Thu 3/28/13	15 days	Mon 3/11/13	Thu 3/28/13
28	Continue demolition of vacant suites on Level 2 & 3	Mon 3/04/13	Fri 3/15/13	26 days	Mon 3/04/13	Fri 4/05/13
29	NIGHT SHIFT - Chip out existing wall / footing and slab at (H2 / 6.5)	Thu 3/21/13	Sat 3/23/13	2 days	Thu 3/21/13	Sat 3/23/13
30	NIGHT SHIFT - Remove Masonry at Gridline 5 (A to B8)	Mon 4/01/13	Fri 4/05/13	5 days	Mon 4/01/13	Fri 4/05/13

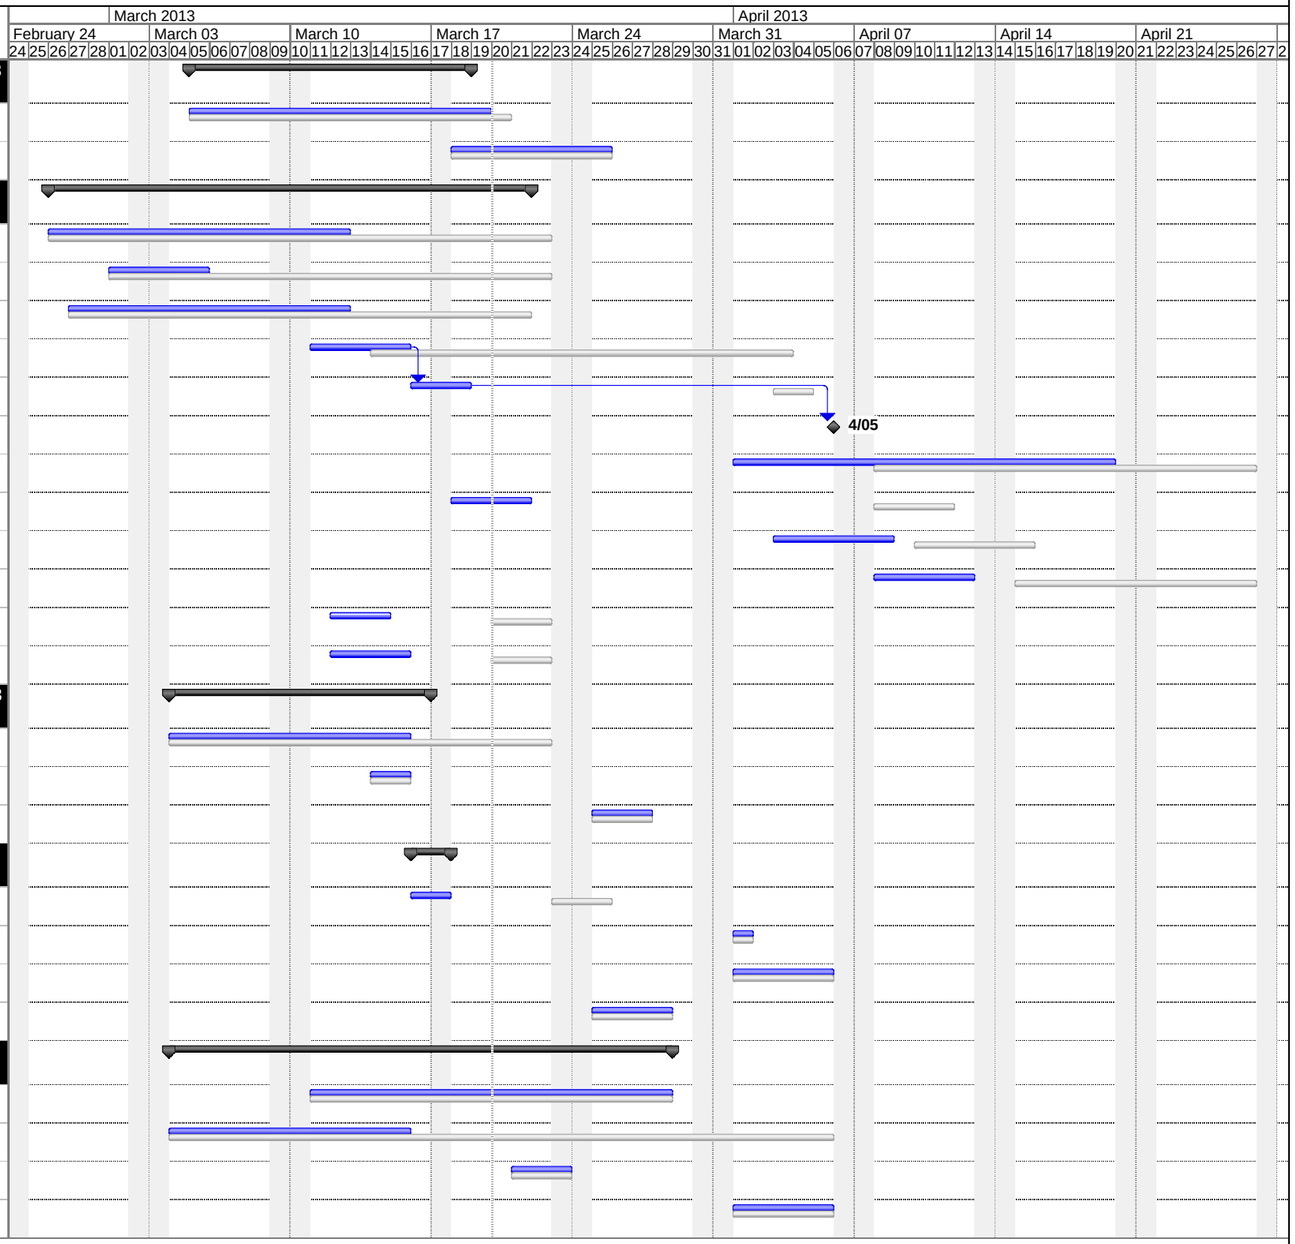

EllisDon
We build on great relationships™

Baseline Task | Actual Progress | Milestone | Summary
